Original/Duplicate/Triplicate

No: First and Part Bill

CONTRACT CERTIFICATE

(For Other Works)

SBRNo: 18/21-22 12/3/2021

Division: **Byatarayanapura** Sub-Division: **Byatarayanapura Sub Division** Date.....20

Received No. Dated Divisional Cash Book Voucher No..... Dated.....

Schedule Docket No. Head of Account: 3075 Sub Divisional **Work Code: 006-21-000009** Est.Cost- **200.00 Lakhs** Indent No 46623

Name of Work: **Improvements to Roads and Drains at Anjanadri Layout Surrounding Area in Ward No 06 Thanisandra**

Name of Contractor and Full Address: **Sri. Vinaya Builders, Prop.Kumar Raju K, No:10 Gokul Nilaya, Dhanalakshmi L/O, Opp Indian Oil Petrol Bank, Thindlu Main Road, Bangalore-97**

Reference to Agreement No: **BBMP/EE/BTP/WO/186/2020-21** Date: 03-02-2021

Certified that the measurements were taken by me on 12.08.2021 and recorded of Pages 49730-44 of measurement Book No. 4974/18-19 .and that the work is satisfactorily executed.

Contractor

Officer-in-charge of work

Certified that the measurement were taken by me on 12/8/0-21 and found correct. The work is satisfactorily executed.

Certified that the quantities of materials shown in column 3 of Account have been actually brought to site of the work and the contractor has not previously received any advance on this security. These materials are of and imperishable nature and are all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal agreement signed and executed by the contractor is recorded in the office.

Sub-Division Officer

II Memorandum of Payment

1) Total value of work done or supplies made as per account within
2) Deduct amount to be held in reserve being .....percent Rs.....
3) " Balance
4) Deduct Payment:
   a) Amount of previous payment as in the Office Cash Book Voucher No.....Dated.....S.D. No.....
      towards cash advance recovery of
   b) Payments Now made { cost store or other material supplied. / recovery of amount creditable to this/other work / Amount paid on this bill Cheque / Cash.
5) Balance being unpaid value of work done held in reserve.
6) Deduct cash advance made on the Office cash Book Voucher No..... dated.....less adjustments.
7) Net amount due to or from Contractor
8) Advance to Contractor for materials brought to site (as detailed) within.
9) Value of Government materials supplied.

Contractor

TTB → 1st & Part Bill	1,36,09,000	00
I+	1,36,090	00
CGST	1,21,509	00
SGST	1,21,509	00
Cess	1,36,090	00
CBF	13,609	00
CR	1,35,003	00
Fine	1,190	00
Deduction	6,65,000	00
Total amount Cheque	1,29,44,000	00

Contractor's Signature

Received Rs..... (in words).....

.....

by cash and by adjustment of Payment as per memorandum (in final settlement of all demands)

P 3075 - Special Comprehensive Development Works in Bangalore city

Witness
1.
2.

Dated Signature of Contractor

Paid by me by Cheque No.....Dated.....

Cash Rs.....

Dated.....

Initials of Officer making payment

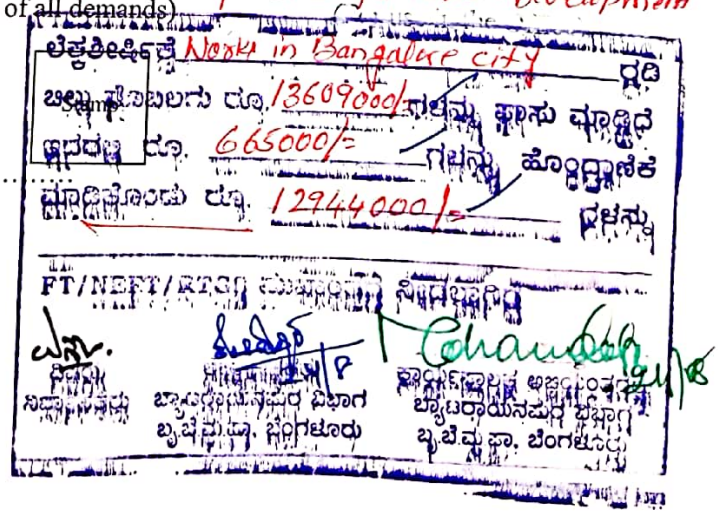

Scanned by CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK: Improvements to Roads and Drains at Anjanadri Layout and Surrounding Area in Ward No 06 Thanisandra

Client	**Sri vinaya Builders Prop.Kumar Raju K No: 10 Gokuka Nilaya, Dhanalakshmi L/O,Opp Indian oil Petrol Bank, Thindlu Main, Road, Bangalore-97**

ABSTRACT

Item no	Description of work	Unit	Modified Approved Schedule-B Qty and rates			Previous			Present			Total Upto Date	
			Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Amount
1	Dismantling of existing structures like culverts,bridges, retaining walls and other structure comprising of masonry, cementconcrete, wood work, steel work, including T&P and scaffolding wherevernecessary, sorting the dismantled material, disposal of unserviceablematerial and stacking the serviceable material with all liftsas per specifications. and as per the directions of the Engineer-in-charge of the work	Cum	0.00	471.91	0	0.00	471.91	0	0.00	471.91	0.00	0.00	0
2	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary, sorting the dismantled material, disposal of unserviceable material and stacking the serviceable material with all lifts complete as per specifications. and as per the directions of the Engineer-in-charge of the work	Cum	0.00	692.57	0	0.00	692.57	0	0.00	692.57	0.00	0.00	0

Scanned by CamScanner

Item no	Description of work	Unit	Modified Approved Schedule-B Qty and rates			Previous			Present			Total Upto Date	
			Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Amount
3	Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications. and as per the directions of the Engineer-in-charge of the work	Cum	1816.77	217.77	395642	0	217.77	0	1814.23	217.77	395088.18 395084.00	1814.23	395088 395084.00
4	Providing and laying Plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with crushed 40mm and down size graded granite metal coarse aggregates @0.89cum and fine aggregates @ 0.46cum, in foundation mechanically mixed, placed in foundation and compacted by vibration including curing for 14 days Including cost of materials,labour, HOM curing form work, Scaffolding and Centering complete as per specifications. and as per the directions of the Engineer-in-charge of the work Quantity upto 125%	Cum	668.88	5692.99	3807927	0	5692.99	0	272.34	5692.99	1550428.00 1550454.52	272.34	1550428.00 1550455
	Quantity above 125%	Cum	38.70	5692.45	220298	0	5692.45	0	0.00	5692.45	0.00	0.00	0

Scanned by CamScanner

Item no	Description of work	Unit	Modified Approved Schedule-B Qty and rates			Previous			Present			Total Upto Date	
			Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Amount
5	Providing laying plain/ reinforced cement concrete for side Drains Using M20 nominal mix Concrete with OPC at 300kgs.With 20mm and Down size granite metal coarse aggregate at 0.69cum and fine aggregate at 0.43cum Machne mixed, well compacted for wall and Bottom including centering shuttering,cost of materials,HOM of Machinery,Curing Etc.,Complete Excluding cost of Steel as per morth MORTH specification and as per the directions of the Engineer-in-charge of the work	Cum	565.59	7423.71	4198776	0	7423.71	0	565.49	7423.71	4198033.00 4198035.25	565.49	4198033.00 4198035
6	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM of machinery complete as per specifications. and as per the directions of the Engineer-in-charge of the work	Tonne	40.61	68299.25	2773632	0	68299.25	0	40.55	68299.25	2769534.00 2769813.15	40.55	2769534.00 2769813

Scanned by CamScanner

Item no	Description of work	Unit	Modified Approved Schedule-B Qty and rates			Previous			Present			Total Upto Date	
			Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Amount
7	Providing and Fixing pre cast covering Slab made out of CC 1:2:4 with 10cm thick and Finishing cutting ,including form work,curing,including cost of alll materials, labour,hire charges of machinery,loading,unloading,lead and lift,transportation etc ,complete.	Sqm	1136.36	2453.85	2788457	0	2453.85	0	1136.36	2453.85	2788457.00 2788456.99	1136.36	2788457
8	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift,transportation etc ,complete and as per the directions of the Engineer-in-charge of the work	Sqm	79.08	5688.90	449878	0	5688.90	0	79.08	5688.90	449879.00 449878.21	79.08	449879.00 449878
9	Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete as per specifications and as per the directions of the Engineer-in-charge of the work Quantity upto 125%	Cum	779.94	59.02	46030	0.00	59.02	0	0	59.02	0.00	0.00	0
	Quantityabove 125%	Cum	525.48	59.07	31040	0.00	59.07	0	0	59.07	59.07	0.00	0

Scanned by CamScanner

Item no	Description of work	Unit	Modified Approved Schedule-B Qty and rates			Previous			Present			Total Upto Date	
			Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Amount
10	Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per specifications. and as per the directions of the Engineer-in-charge of the work Quantity upto 125%	Sqm	1733.19	6.36	11023	0.00	6.36	0	0	6.36	0.00	0.00	0
	Quantityabove 125%	Sqm	1167.74	6.68	7801	0.00	6.68	0	0	6.68	0.00	0.00	0
11	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site, spreading in uniform layers with motor grader on prepared surface and compacting with vibratory power roller to achieve the 98 % proctor density, complete as per specifications and as per the directions of the Engineer-in-charge of the work Quantity upto 125%	Cum	259.98	2090.68	543534	0.00	2090.68	0	0	2090.68	0.00	0.00	0
	Quantityabove 125%	Cum	175.16	2094.47	366867	0	2094.47	0	0	2094.47	2094.47	0.00	0

Scanned by CamScanner

Item no	Description of work	Unit	Modified Approved Schedule-B Qty and rates			Previous			Present			Total Upto Date	
			Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Amount
12	Cement concrete pavement.Construction of un-reinforced plain cement concrete pavement, using a grade concrete M30 over a prepared base with OPC coarse aggregate @ 0.69cum fine aggregate @ 0.46cum.coarse and fine aggregate confirming to IS:383-2016,with superplastisiser @3lts confirming to IS9103-2008mixed in a concrete mixer of not less than 0.6 cum capacity and appropriate weigh batcher as per approved mix design, laid in approved fixed side form work (steel channel, laying and fixing of 125 micron thick polythene film, wedges, steel plates including levelling the form work as per drawing). Spreading the concrete with shovels, rackers compacted using needle, screed and plate vibrator and finished in a continuous operation including provision of contraction, expansion, construction and longitudinal joints including groove cutting charges, joint filler, separation membrane, selant	Cum	259.98	5471.51	1422483	0.00	5471.51	0	0	5471.51	0.00	0.00	0
	Quantity above125%	Cum	175.16	5470.99	958299	0.00	5470.99	0	0	5470.99	0.00	0.00	0

Scanned by CamScanner

Item no	Description of work	Unit	Modified Approved Schedule-B Qty and rates			Previous			Present			Total Upto Date	
			Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Amount
E1	Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in Ordinary soil not exceeding 1.5m in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50m after breaking of clods complete as per specifications and directions of the Engineer in charge.	Cum	246.96	332.76	82178	0.00	332.76	0	0	332.76	0.00	0.00	0
E2	Providing and installing at site of work 63mm (0.662) PVC Pipes of 6kg / cm2 including cost of pipes and specials and labour, including lowering into trenches, laying true to line, level and perfect linking at joints leak proof including joining of approved type with all labour and lift charges, handling charges including encasing the pipe alround to a depth not less than 15cms with gravel or selected earth available from the excavation etc., complete as per	m	548.8	414.00	227203	0.00	414.00	0	0	414.00	0.00	0.00	0

Scanned by CamScanner

Item no	Description of work	Unit	Modified Approved Schedule-B Qty and rates			Previous			Present			Total Upto Date	
			Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Rate	Amount	Qnty	Amount
E3	Refilling available earth around pipe lines, cables in layers not exceeding 20cms in depth, compacting each deposited layer by ramming after watering with lead upto 50m and lift upto 1.5m including cost of all labour complete as per specifications and directions of the Engineer in charge.	Cum	246.96	134.66	33256	0.00	134.66	0	0	134.66	0.00	0.00	0
	Total Amount				18364324						12151726		12151726.3
	GST 12%				2203719						1458207		1458207
	Grand Total amount				20568043						13609933		13609933

Certificate

1.The Work executed by the contractor is found satisfactory

2. The contractor has removed the debris from the work spot

3. There are no departmental issues for this work

Sub total : 1,21,51,415.00

GST 12% : 14,58,169.80

total : 1,36,09,584.80

Rand off : 1,36,09,000.00

Contractor

Assistant Engineer

Assistant Executive Engineer

Scanned by CamScanner

Original/Duplicate/Triplicate

CONTRACT CERTIFICATE

(For Other Works)

SBR No: 18/21-22 Date: 12/3/2021

No: First and Part Bill

Division: **Byatarayanapura** Sub-Division: **Byatarayanapura Sub Division**

Received No. Dated Divisional Cash Book Voucher No..... Dated.....

Sub Divisional **Work Code: 006-21-000009** Indent No 46623

Schedule Docket No. Head of Account: 3075 Est.Cost- **200.00 Lakhs**

Name of Work: **Improvements to Roads and Drains at Anjanadri Layout Surrounding Area in Ward No 06 Thanisandra**

Name of Contractor and Full Address: **Sri. Vinaya Builders, Prop.Kumar Raju K, No:10 Gokul Nilaya, Dhanalakshmi L/O, Opp Indian Oil Petrol Bank, Thindlu Main Road, Bangalore-97**

Reference to Agreement No: **BBMP/EE/BTP/WO/186/2020-21** Date: 03-02-2021

Certified that the measurements were taken by me on 12.08.2021 and recorded of Pages 49734o-44 of measurement Book No. 4974 18-19 .and that the work is satisfactorily executed.

Contractor

Officer-in-charge of work

Certified that the measurement were taken by me on 12.8.21 and found correct. The work is satisfactorily executed.

Certified that the quantities of materials shown in column 3 of Account have been actually brought to site of the work and the contractor has not previously received any advance on this security. These materials are of and imperishable nature and are all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal agreement signed and executed by the contractor is recorded in the office.

Sub-Division Officer

II Memorandum of Payment

1) Total value of work done or supplies made as per account within
2) Deduct amount to be held in reserve being .....percent Rs.....
3) " Balance
4) Deduct Payment:
   a) Amount of previous payment as in the Office Cash Book Voucher No.....Dated.....S.D. No.....
   towards cash advance recovery of
   b) Payments Now made { cost store or other material supplied. / recovery of amount creditable to this/other work / Amount paid on this bill Cheque / Cash.
5) Balance being unpaid value of work done held in reserve.
6) Deduct cash advance made on the Office cash Book Voucher No..... dated.....less adjustments.
7) Net amount due to or from Contractor
8) Advance to Contractor for materials brought to site (as detailed) within.
9) Value of Government materials supplied.

TTB →

1st & Post Bill	1,36,09,000	00
Add: 1%	1,36,090	00
CGST	1,21,509	00
SGST	1,21,509	00
Cess	1,36,090	00
CBF	13,609	00
LR	1,35,003	00
Fine	1,190	00
Deductions	6,65,000	00
Total amount Cheque	1,29,44,000	00

Contractor

Received Rs..... (in words).....

.....

by cash and by adjustment of Payment as per memorandum (in final settlement of all demands)

P 3075 - Special Comprehensive Development Works in Bangalore city

Witness
1.
2.

Dated Signature of Contractor

Paid by me by Cheque No.....Dated.....

Cash Rs.....

Dated.....

Initials of Officer making payment

Scanned by CamScanner
